ID	% Work Complete	Task Name	Duration	Start	Finish	Actual Start	Actual Finish	Predecessors	Successors
1	**0%**	**PRECONSTRUCTION**	**43 days**	**Mon 7/6/26**	**Wed 9/2/26**	**Mon 7/6/26**	**NA**		
6	25%	Submittals Review and Approve	15 days	Thu 8/13/26	Wed 9/2/26	Thu 8/13/26	NA	5	
7	**0%**	**CONSTRUCTION**	**67 days**	**Mon 8/3/26**	**Wed 11/4/26**	**Mon 8/3/26**	**NA**		
8	**0%**	**Sitework**	**54 days**	**Mon 8/3/26**	**Fri 10/16/26**	**Mon 8/3/26**	**NA**		
13	100%	Demoltion of Concrete	3 days	Thu 8/13/26	Mon 8/17/26	Thu 8/13/26	Mon 8/17/26	12	14
14	100%	Demolition Complete	0 days	Mon 8/17/26	Mon 8/17/26	Mon 8/17/26	Mon 8/17/26	13	15
15	10%	Rough Site Grading	4 days	Mon 8/17/26	Fri 8/21/26	Mon 8/17/26	NA	14	16,20
16	20%	Underground Storm Lines and Inlets	10 days	Tue 8/18/26	Fri 9/4/26	Tue 8/18/26	NA	15	17SS+5 days,18SS+7 da
17	0%	Tie Gutters into Roof Drain System	2 days	Tue 8/25/26	Wed 8/26/26	NA	NA	16SS+5 days	18
18	0%	Install Underdrain Behind Curb and Gutter	2 days	Thu 8/27/26	Fri 8/28/26	NA	NA	16SS+7 days,17	19
19	0%	Storm Water Complete	0 days	Fri 8/28/26	Fri 8/28/26	NA	NA	18	
20	0%	Excavate Under Garages	2 days	Mon 8/24/26	Tue 8/25/26	NA	NA	15	21
21	0%	Install Micropiles and Void Forms	4 days	Wed 8/26/26	Mon 8/31/26	NA	NA	20	22
22	0%	Micropiles Complete	0 days	Mon 8/31/26	Mon 8/31/26	NA	NA	21	23
23	0%	Site Grading	5 days	Tue 9/1/26	Tue 9/8/26	NA	NA	22	24

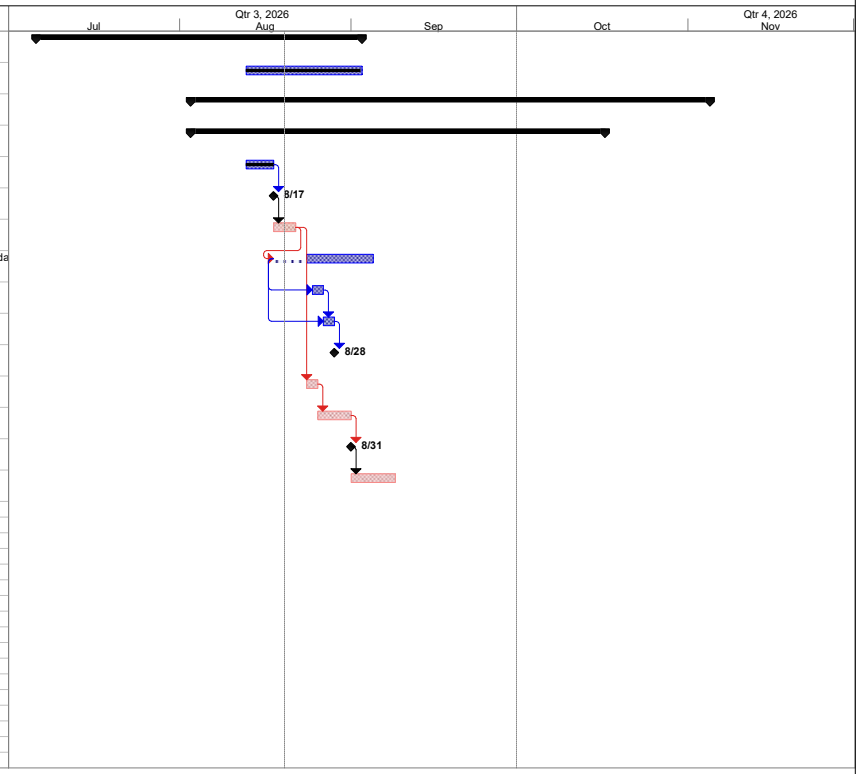

McCauley CONSTRUCTORS

Task		Project Summary		Inactive Milestone		Duration-only		Finish-only		Critical Split			
Split		External Tasks		Inactive Milestone		Manual Summary Rollup		External Tasks		Progress			
Milestone		External Milestone		Inactive Summary		Manual Summary		External Milestone		Deadline			
Summary		Inactive Task		Manual Task		Start-only		Critical					
